

EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010 FIRE STATION NO. 5 REPLACEMENT

This project will provide a new seismically safe facility for the San Francisco Fire Department.

GENERAL INFORMATION

Project Updates

- Gypsum sheathing and weatherproofing at the west and east exterior elevations is complete.
- Set skylight curbs, mechanical unit curbs, roof hatch, and through wall scuppers at roof.
- No weekend work is scheduled to occur on Saturday, 6/9.

Activities Week of 6/11/2018 - 6/16/2018

- Finish installation of gypsum sheathing and weatherproofing at the north and south exterior elevations.
- Installation of tapered insulation and cover board at roof.
- Finish installation of interior metal stud framing at 1st floor.
- Installation of curtainwall at north, east, and south exterior elevations.
- Weekend work is tentatively scheduled to occur on Saturday, 6/16.


Activities Week of 6/18/2018 - 6/23/2018

- Finish installation of cover board at roof and begin installation of fluid-applied roofing system.
- Installation of curtainwall at north, east, and south exterior elevations.
- Weekend work is tentatively scheduled to occur on Saturday, 6/23.

Other Information

- SFFD is responding from nearby Fire Stations 6 and 38; fire service will continue uninterrupted. sf-fire.org/temporary-fire-station-closure-service-status
- View construction progress photos and subscribe to this
- newsletter: <u>sfearthquakesafety.org/firestation5</u>

Skylight and Mechanical Unit Curbs Set at Roof (June 6, 2018)

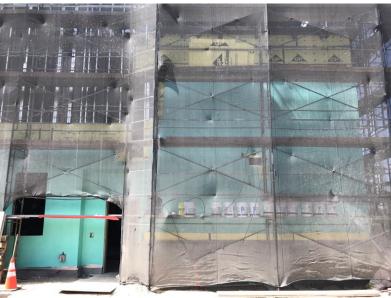

Gypsum Sheathing and Waterproofing at South Exterior Elevation (June 6, 2018)

К	
	FALL 2018
» Generator and Elevator	» Substantial completion
 Interior work and Site Utilities 	 » SFFD move-in
For immediate service regarding	For emergencies:
construction issues:	
Ray Birmingham, Construction Manager	Alten Construction
Ray.Birmingham@sfdpw.org	Harry Torrano, Site Superintendent
(415) 244-9748	(415) 559-6063
	B 2018 » Generator and Elevator » Interior work and Site Utilities For immediate service regarding construction issues: Ray Birmingham, Construction Manager Ray.Birmingham@sfdpw.org

SCHEDULE

» Interior work

lssue #21 June 8, 2018
